

# 30-DAY OPERATIONS PLAN (30D PLAN)

## General Information

Item : Description

Business Unit : Corridor Asset

Area / Facility : Suban

30D Period : 01-30 July 2026

Document Status : ☐ Draft ☐ Reviewed ☐ Frozen (Approved)

Issue Date : 29 June 2026

Revision : 0

## 1. EXECUTIVE DECISION SUMMARY

### 1.1 Top Priority & Decision-Driving Activities

*(Focus on activities requiring management decision)*

| No | Activity                                                                                                             | Area  | Primary Impact<br>(Production /<br>HSE / Integrity<br>/ Cost) | MWC      | Key Risk                         | Management<br>Decision                |
|----|----------------------------------------------------------------------------------------------------------------------|-------|---------------------------------------------------------------|----------|----------------------------------|---------------------------------------|
| 1  | REPLACE SURGE<br>ARRESTER DCS AND SIS<br>SUBAN                                                                       | Suban | Reliability                                                   | Electric | Electrical failure               | Approved to<br>execute as<br>planned. |
| 2  | Dismantling/Relocation<br>Existing Metering Suban<br>to Rawa Station                                                 | Suban | Production                                                    | OCS      | Lifting                          | Approved to<br>execute as<br>planned. |
| 3  | Construct New Water<br>Well Suban Sumur<br>Pantau. Install AWLR<br>(Automatic Water Level<br>Recorder).              | Suban | Regulatory                                                    | Offsite  | Trip, slip, fall, drop<br>object | Approved to<br>execute as<br>planned. |
| 4  | Suban 24 Flowline<br>Construction. Hydrotest<br>underground flowline,<br>Hot tap welding, DCS<br>panel modification. | Suban | Production                                                    | Project  | Lifting, Hot work                | Approved to<br>execute as<br>planned. |

|    |                                                                                                |       |             |                                    |                                                                              |                                 |
|----|------------------------------------------------------------------------------------------------|-------|-------------|------------------------------------|------------------------------------------------------------------------------|---------------------------------|
| 5  | Coating Repair Follow Up IAAN Verification Flowline SBN#8 (3 Cluster)                          | Suban | Integrity   | Offsite                            | Chemical hazard                                                              | Approved to execute as planned. |
| 6  | Debottlenecking Suban 7. Install 1 quill tubing, Install bypass choke valve                    | Suban | Production  | OCS                                | Need isolate degassing#3 and #4 during execution                             | Approved to execute as planned. |
| 7  | Dismantle Inlet separator and accessories. Scanning and dismantle instrumentation accessories. | Suban | Production  | OCS: Electric, Instrument          | WAH                                                                          | Approved to execute as planned. |
| 8  | Suban Flowline Derating Modification. Modification 2 PSV                                       | Suban | Cost        | OCS                                | Lifting, WAH                                                                 | Approved to execute as planned. |
| 9  | Suban-5 SRU Installation                                                                       | Suban | Production  | Engineering: OCS, Mechanic, Vendor | Production impact during execution                                           | Approved to execute as planned. |
| 10 | Suban-13 Acidizing                                                                             | Suban | Production  | WII & Offsite                      | Production impact during execution                                           | Approved to execute as planned. |
| 11 | Retrofit 247-PBC-204A SB_DT315292 (Battery Charger PCR#2                                       | Suban | Reliability | Electric Specialist                | Battery system failure causing loss of backup power for critical instruments | Approved to execute as planned. |
| 12 | 4K GTC-500 PM                                                                                  | Suban | Production  | Campaign                           | Production impact during execution                                           | Approved to execute as planned. |
| 13 | Construct New Water Well Suban-6. Permit processing                                            | Suban | Regulatory  | Offsite                            | Trip, slip, fall, drop object                                                | Approved to execute as planned. |
| 14 | Tuning engine performance GTC-300                                                              | Suban | Reliability | FREE                               | Trip, slip, fall                                                             | Approved to execute as planned. |
| 15 | ASM verification                                                                               | Suban | Regulatory  | Offsite                            | Animal hazard                                                                | Approved to execute as planned. |

## 1.2 Key Decisions for the Month

### ☐ Activities approved for execution (Frozen)

- All activities listed under Section-2 have been approved and frozen as the execution commitment.

☐ Activities deferred / rephased: -

☐ Activities rejected: -

### 1.3 Early Warning & Look-Ahead (Next 30–60 Days)

## 2. 30D ACTIVITY LIST – FROZEN (EXECUTION COMMITMENT)

*Note: Only activities that have met all readiness requirements are allowed in this section.*

### Activity Highlight

| No | Activity                                                                                                 | Category    | Area  | Job Owner                          | Start Date   | End Date     | Remark                                                         |
|----|----------------------------------------------------------------------------------------------------------|-------------|-------|------------------------------------|--------------|--------------|----------------------------------------------------------------|
| 1  | REPLACE SURGE ARRESTER DCS AND SIS SUBAN                                                                 | Reliability | Suban | Electric                           | 19 July 2026 | 19 July 2026 |                                                                |
| 2  | Dismantling/Relocation Existing Metering Suban to Rawa Station                                           | Production  | Suban | OCS                                | 15 July 2026 | 20 July 2026 | Duration: half day                                             |
| 3  | Construct New Water Well Suban Sumur Pantau. Install AWLR (Automatic Water Level Recorder).              | Regulatory  | Suban | Offsite                            | 1 July 2026  | 7 July 2026  |                                                                |
| 4  | Suban 24 Flowline Construction. Hydrotest underground flowline, Hot tap welding, DCS panel modification. | Production  | Suban | Project                            | 1 July 2026  | 31 July 2026 | Need MOC for DCS panel modification.                           |
| 5  | Coating Repair Follow Up IAAN Verification Flowline SBN#8 (3 Cluster)                                    | Integrity   | Suban | Offsite                            | 1 July 2026  | 6 July 2026  |                                                                |
| 6  | Debottlenecking Suban 7. Install 1 quill tubing, Install bypass choke valve                              | Production  | Suban | OCS                                | 3 July 2026  | 31 July 2026 |                                                                |
| 7  | Dismantle Inlet separator and accessories. Scanning and dismantle instrumentation accessories.           | Production  | Suban | OCS: Electric, Instrument          | 7 July 2026  | 25 July 2026 | Scanning, Dismantle Instrumentation accessories                |
| 8  | Suban Flowline Derating Modification. Modification 2 PSV                                                 | Cost        | Suban | OCS                                | 15 July 2026 | 31 July 2026 |                                                                |
| 9  | Suban-5 SRU Installation                                                                                 | Production  | Suban | Engineering: OCS, Mechanic, Vendor | 5 July 2026  | 12 July 2026 | Need Scaffolding, Crane, Manpower from Maintenance & Operation |
| 10 | Suban-13 Acidizing                                                                                       | Production  | Suban | WII & Offsite                      | 3 July 2026  | 14 July 2026 | Need support from Offsite for                                  |

|    |                                                           |             |       |                     |             |              |                   |
|----|-----------------------------------------------------------|-------------|-------|---------------------|-------------|--------------|-------------------|
|    |                                                           |             |       |                     |             |              | flange management |
| 11 | Retrofit 247-PBC-204A SB_DT315292 (Battery Charger PCR#2) | Reliability | Suban | Electric Specialist | 8 July 2026 | 15 July 2026 |                   |
| 12 | 4K GTC-500 PM                                             | Production  | Suban | Campaign            | 5 July 2026 | 6 July 2026  |                   |
| 13 | Construct New Water Well Suban-6. Permit processing       | Regulatory  | Suban | Offsite             | 8 July 2026 | 31 July 2026 |                   |
| 14 | Tuning engine performance GTC-300                         | Reliability | Suban | FREE                | 4 July 2026 | 4 July 2026  |                   |
| 15 | ASM verification                                          | Regulatory  | Suban | Offsite             | 1 July 2026 | 10 July 2026 |                   |

### Equipment Certification:

| NO. | ACTIVITY                                 | DEPT    | REMARK                                |
|-----|------------------------------------------|---------|---------------------------------------|
| 1   | HC02 4Y-CERTIFICATION MIGAS PSV QA PM    | QC      | SUBAN                                 |
| 2   | HC02 4Y-CERTIFICATION MIGAS PSV QA PM    | QC      | VALVE, PRESSURE SAFETY OUTLET 229V103 |
| 3   | 4Y-CERTIFICATION MIGAS PSV QA PM         | QC      | SUBAN                                 |
| 4   | 4Y-CERTIFICATION MIGAS PSV QA PM         | QC      | COMPRESSED AIR                        |
| 5   | 4Y-CERTIFICATION MIGAS PSV QA PM         | QC      | CHEMICAL INJECTION                    |
| 6   | 4Y-CERTIFICATION MIGAS PSV QA PM         | QC      | VALVE,PRESSURE SAFETY OF 67MBK302B    |
| 7   | Persetujuan Layak Operasi (PLO) Suban-34 | Project | Suban-34 Well and Flowline            |

### 3. CONDITIONAL / AT-RISK ACTIVITIES (NOT APPROVED FOR EXECUTION)

*Activities listed below are NOT approved for execution and are shown for visibility and readiness monitoring only.*

| No | Activity | Reasons Not Ready | Required Action | Target Date | PIC |
|----|----------|-------------------|-----------------|-------------|-----|
| -  | -        | -                 | -               | -           | -   |

### 4. MOC-RELATED ACTIVITIES

| No | Activity                                                                   | Area  | MOC Status | Operational Impact           | Decision                              |
|----|----------------------------------------------------------------------------|-------|------------|------------------------------|---------------------------------------|
| 1  | Suban 24 New Flowline Early Work. PID: 10222322                            | Suban | Execution  | Worksite Coordination        | Approved – execute under approved MOC |
| 2  | SB-07 Debottlenecking. PID: 9485638                                        | Suban | Execution  | Potential Production impact  | Approved – execute under approved MOC |
| 3  | KOH Injection Facility at Produced Water System (Permanent). PID: 10069112 | Suban | Execution  | No direct production impact  | Approved – execute under approved MOC |
| 4  | Construct New Water Wells at Suban. PID: 9691419                           | Suban | Execution  | No production impact, impact | Approved – execute under approved     |

|    |                                                                                                  |       |                                                   |                                   |                                       |
|----|--------------------------------------------------------------------------------------------------|-------|---------------------------------------------------|-----------------------------------|---------------------------------------|
|    |                                                                                                  |       |                                                   | to standard government regulation | MOC. Follow up due in 30D             |
| 5  | Suban-24 New Flowline Full Scope. PID: 10321684                                                  | Suban | Execution                                         | Worksite Coordination             | Approved – execute under approved MOC |
| 6  | Condensate Metering Relocation to Ramba for Aktivitas Sumur Masyarakat (235-A-101). PID: 9991893 | Suban | Execution                                         |                                   | Approved – execute under approved MOC |
| 7  | Suban Well Instrument Gas Replacement. PID: 10324913                                             | Suban | Execution                                         | Potential operational risk        | Approved – execute under approved MOC |
| 8  | Equipment Dismantling for Sakakemang Project. PID: 10374495                                      | Suban | Execution                                         | Potential operational risk        | Follow up approval MOC                |
| 9  | Rental Solid Removal Unit for SB-05. PID: 10634155                                               | Suban | Corrective Action Review by Surveillance Engineer | Production impact                 | Follow up approval MOC                |
| 10 | Derating PSV Inlet Header Suban                                                                  | Suban | Execution                                         | Potential operational risk        | Approved – execute under approved MOC |

## 5. SIMOPS, LIFTING & SCAFFOLDING CONTROL


### 5.1 SIMOPS & Critical Overlap

| Area | Period | Concurrent Activities | Risk | Control / Mitigation |
|------|--------|-----------------------|------|----------------------|
| -    | -      | -                     | -    | -                    |

### 5.2 Scanning and Excavation Activities

| Area                    | Period  | Type     | Concurrent Activities                                                          | Risk                                     | Control / Mitigation                   |
|-------------------------|---------|----------|--------------------------------------------------------------------------------|------------------------------------------|----------------------------------------|
| Suban Plant (Electric)  | W1 July | Scanning | Dismantle Inlet separator and accessories, road and area for crane improvement | Underground facility, personnel exposure | Barricade, permit control, supervision |
| Suban Offsite (Offsite) | W1 July | Scanning | Suban 24 Installation - Civil - Trenching ROW Line                             | Underground facility, personnel exposure | Barricade, permit control, supervision |
| Suban Offsite (Offsite) | W1 July | Scanning | Suban 24 Installation - Piping - Lowering & Backfilling Pipeline               | Underground facility, personnel exposure | Barricade, permit control, supervision |
| Suban Offsite (Offsite) | W1 July | Scanning | Scanning for Suban 24 Installation - Civil - Trenching ROW Line                | Underground facility, personnel exposure | Barricade, permit control, supervision |

|                         |              |                       |                                                                                          |                                          |                                        |
|-------------------------|--------------|-----------------------|------------------------------------------------------------------------------------------|------------------------------------------|----------------------------------------|
| Suban Offsite (Offsite) | W1 July      | Scanning              | Scanning for Suban 24 Installation - Piping - Lowering & Backfilling Pipeline            | Underground facility, personnel exposure | Barricade, permit control, supervision |
| Suban Offsite (Offsite) | W1 – W5 July | Mechanical Excavation | FOLLOW UP IAAN IP VERIFICATION RESULT SUBAN 8 FLOWLINE CLUSTER 4 : MECHANICAL EXCAVATION | Underground facility, personnel exposure | Barricade, permit control, supervision |
| Suban Offsite (Offsite) | W1 July      | Mechanical Excavation | FOLLOW UP IAAN IP VERIFICATION RESULT SUBAN 8 FLOWLINE CLUSTER 5 : MECHANICAL EXCAVATION | Underground facility, personnel exposure | Barricade, permit control, supervision |
| Suban Offsite (Offsite) | W1 July      | Mechanical Excavation | FOLLOW UP IAAN IP VERIFICATION RESULT SUBAN 8 FLOWLINE CLUSTER 6 : MECHANICAL EXCAVATION | Underground facility, personnel exposure | Barricade, permit control, supervision |
| Suban Offsite (Offsite) | W1 July      | Mechanical Excavation | Install New Test Point 26in Gas & 8in Condensate KP3 (From Suban): Mechanical Excavation | Underground facility, personnel exposure | Barricade, permit control, supervision |
| Suban Offsite (Offsite) | W1 July      | Mechanical Excavation | Install New Test Point 26in Gas & 8in Condensate KP4 (From Suban): Mechanical Excavation | Underground facility, personnel exposure | Barricade, permit control, supervision |

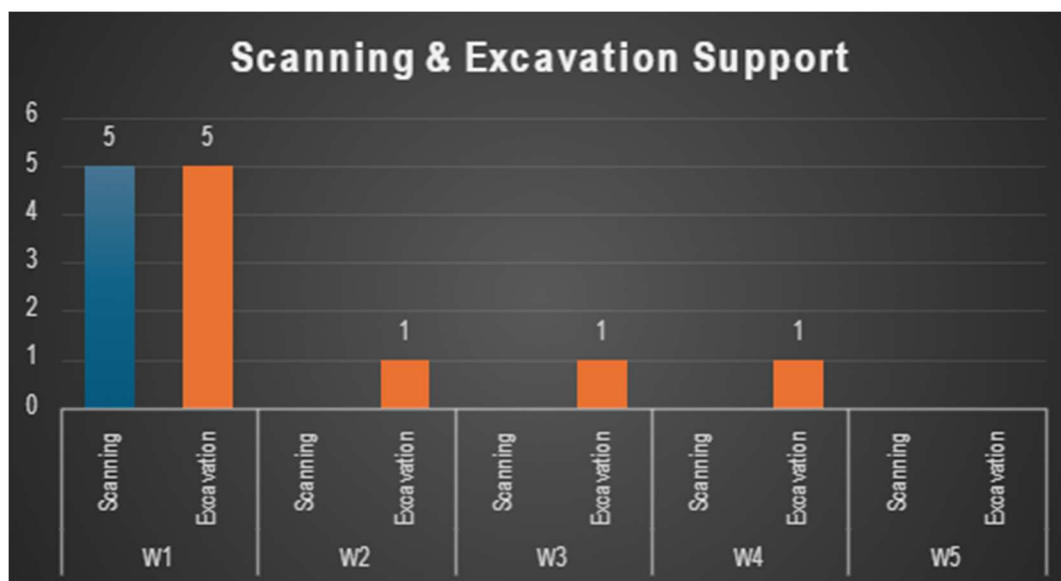


## 5.2 Lifting & Scaffolding Summary

| Activity                                                                                                   | Area          | Period  | Type (Lifting / Scaffold) | Risk Class | SIMOPS (Yes/No) |
|------------------------------------------------------------------------------------------------------------|---------------|---------|---------------------------|------------|-----------------|
| Repair Air Inlet Housing at Residue comp                                                                   | Suban Plant   | W5      | Lifting                   | Medium     | No              |
| PROD WATER PUMP 258P202B LOW PERFORM                                                                       | Suban Plant   | W1      | Lifting                   | Medium     | No              |
| Follow up finding COMO replace pump bearing condensate pump 235-P-102-E SBCP                               | Suban Plant   | W1      | Lifting                   | Medium     | No              |
| Overhaul Produced WIP 258P102B                                                                             | Suban Plant   | W1      | Lifting                   | Medium     | No              |
| Suban 24 Installation - Piping - Hot Tap                                                                   | Suban Offsite | W2 – W4 | Lifting                   | High       | No              |
| Debottlenecking Suban 7                                                                                    | Suban Plant   | W1-W2   | Lifting                   | High       | No              |
| Suban-5 SRU Installation                                                                                   | Suban Well    | W2      | Lifting                   | Medium     | No              |
| 20 EA LAMPS AT AMINE AREA SHUT OFF                                                                         | Suban Plant   | W-5     | Scaffolding               | Medium     | No              |
| RDG: LAMPS AT GLYCOL AREA OFF                                                                              | Suban Plant   | W-5     | Scaffolding               | Medium     | No              |
| AIR TERMINAL BUILDG BLOK D CAMP-2 BROKEN                                                                   | Suban Offsite | W-1     | Scaffolding               | Medium     | No              |
| Repair Air Inlet Housing at Residue comp                                                                   | Suban Plant   | W-5     | Scaffolding               | Medium     | No              |
| EDSFDG: 250-LT-2211 have alert                                                                             | Suban Plant   | W-2     | Scaffolding               | Medium     | No              |
| 1Y-CONTROL VALVE: STROKE TEST FOR PROPER                                                                   | Suban Plant   | W-3     | Scaffolding               | High       | No              |
| 1Y-SWITCH: FUNCTION TEST                                                                                   | Suban Plant   | W-3     | Scaffolding               | High       | No              |
| 2Y-230LT352: FUNCT.TEST                                                                                    | Suban Plant   | W-4     | Scaffolding               | High       | No              |
| 1Y-SWITCH: FUNCTION TEST                                                                                   | Suban Plant   | W-4     | Scaffolding               | High       | No              |
| 2Y-230LT2332: FUNCT TEST                                                                                   | Suban Plant   | W-5     | Scaffolding               | High       | No              |
| Coating New Bottom Plate Venturi Air Inlet Housing GTC-401                                                 | Suban Plant   | W-1     | Scaffolding               | High       | No              |
| Flare Stack Inspection                                                                                     | Suban Plant   | W-5     | Scaffolding               | Medium     | No              |
| Install Scaffolding at Roof for repair AIR TERMINAL BUILDG BLOK D CAMP-2 BROKEN                            | Suban Plant   | W-4     | Scaffolding               | Medium     | No              |
| Install scaffolding for support Acidizing activity at Suban-13 Well                                        | Suban Plant   | W-4     | Scaffolding               | Medium     | No              |
| Install sacffolding for support Migas PSV recertification 215PSV101                                        | Suban Plant   | W-2     | Scaffolding               | Medium     | No              |
| Install sacffolding for support Migas PSV recertification 225PSV2281                                       | Suban Plant   | W-2     | Scaffolding               | Medium     | No              |
| Install scaffolding for installing Roofing shelter travo, Depan Warehouse shelter C area/ Mechanic Shop    | Suban Plant   | W-3     | Scaffolding               | Medium     | No              |
| Install scaffolding untuk lantai kerja di area ducting kitchen hood di bagian atap rechall PERmanent camp. | Suban Offsite | W-4     | Scaffolding               | Medium     | No              |
| Dismantle Fire monitor support near Glycol Area                                                            | Suban Plant   | W-1     | Scaffolding               | Medium     | No              |

|                                                                                                          |               |     |             |        |    |
|----------------------------------------------------------------------------------------------------------|---------------|-----|-------------|--------|----|
| Reinstall Fire monitor support near Glycol Area using Scaffolding pipe                                   | Suban Plant   | W-1 | Scaffolding | Medium | No |
| Install scaffolding for replace roofing shelter travo mechanic workshop offsite area                     | Suban Offsite | W-3 | Scaffolding | Medium | No |
| Install PSV and anchor point PSV certification 3LPSV0007                                                 | Suban Plant   | W-5 | Scaffolding | Medium | No |
| Install scaffolding for support isolation degassing column 301/401(modification injection point for KOH) | Suban Plant   | W-5 | Scaffolding | Medium | No |
| Install Scaffolding for replace& install roofing                                                         | Suban Offsite | W-1 | Scaffolding | Medium | No |
| Install Scaffolding at suban well 5                                                                      | Suban Well    | W-1 | Scaffolding | Medium | No |
| Install scaffolding for 1Y LTS 230V101 INS PM                                                            | Suban Plant   | W-3 | Scaffolding | Medium | No |
| Install scaffolding for SS04 1Y LTS 230V101 INS PM                                                       | Suban Plant   | W-3 | Scaffolding | Medium | No |
| Install scaffolding for 2Y LTS 230V201 INS PM                                                            | Suban Plant   | W-4 | Scaffolding | Medium | No |
| Install scaffolding for SS04 1Y LTS 230V201 INS PM                                                       | Suban Plant   | W-4 | Scaffolding | Medium | No |
| Install scaffolding for 2Y LTS 230V301 INS PM                                                            | Suban Plant   | W-5 | Scaffolding | Medium | No |
| Install scaffolding for EDSFDG: 250-LT-2211 have alert                                                   | Suban Plant   | W-2 | Scaffolding | Medium | No |
| 4M-CONDENSATE SHIPPING PUMP "B" MEC PM                                                                   | Suban Plant   | W-1 | Scaffolding | Medium | No |
| HAND WHEEL OF 3/4 GLOBE VALVE BROKEN                                                                     | Suban Plant   | W-1 | Scaffolding | Medium | No |
| REPAIR AIR INLET HOUSING GTC-401                                                                         | Suban Plant   | W-2 | Scaffolding | Medium | No |
| RDG: COATING APPLY ON WELDOLET LEAN AMIN                                                                 | Suban Plant   | W-1 | Scaffolding | Medium | No |
| RDG: 20 EA LAMPS AT AMINE AREA SHUT OFF                                                                  | Suban Plant   | W-2 | Scaffolding | Low    | No |
| RDG: LAMPS AT GLYCOL AREA OFF                                                                            | Suban Plant   | W-2 | Scaffolding | Low    | No |
| AIR TERMINAL BUILDG BLOK D CAMP-2 BROKEN                                                                 | Suban Offsite | W-2 | Scaffolding | Low    | No |
| HAND WHEEL OF 3/4 GLOBE VALVE BROKEN                                                                     | Suban Plant   | W-2 | Scaffolding | Low    | No |
| REPAIR AIR INLET HOUSING GTC-401                                                                         | Suban Plant   | W-2 | Scaffolding | Medium | No |
| EDSFDG: 250-LT-2211 have alert                                                                           | Suban Plant   | W-2 | Scaffolding | Low    | No |
| 1Y LTS 230V101 INS PM                                                                                    | Suban Plant   | W-2 | Scaffolding | High   | No |
| SS04 1Y LTS 230V101 INS PM                                                                               | Suban Plant   | W-2 | Scaffolding | High   | No |
| 2Y LTS 230V201 INS PM                                                                                    | Suban Plant   | W-2 | Scaffolding | High   | No |
| SS04 1Y LTS 230V201 INS PM                                                                               | Suban Plant   | W-2 | Scaffolding | High   | No |
| 2Y LTS 230V301 INS PM                                                                                    | Suban Plant   | W-2 | Scaffolding | High   | No |



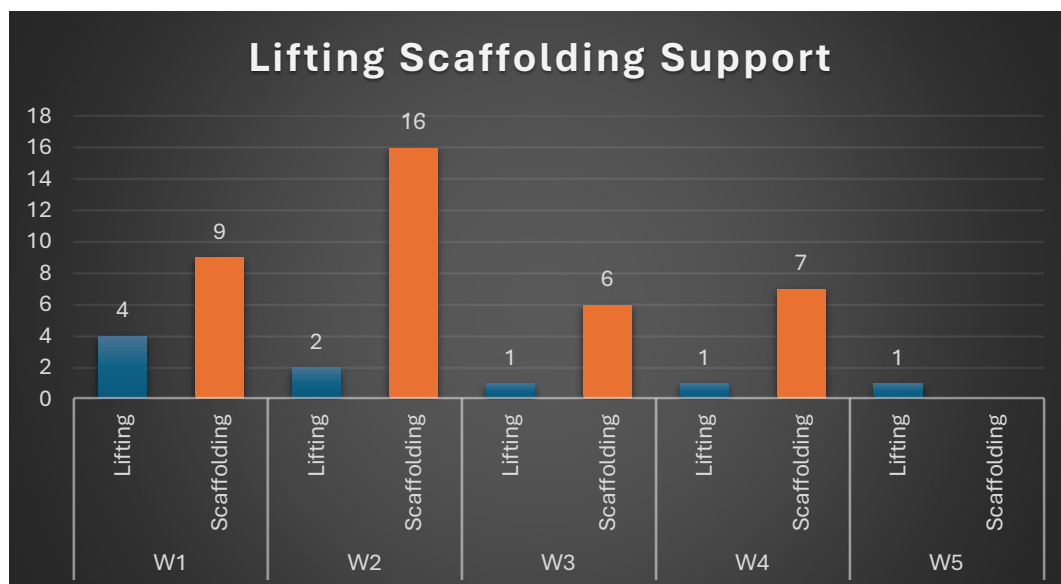

\*Assumed scaffolding risk classification:

- Working height greater than 5 meters (>5m) is classified as Medium Risk.
- Working height equal to or less than 5 meters (<5m) is classified as Low Risk.

## 5.3 Manpower

| Activity                                                       | Area       | Manpower       |
|----------------------------------------------------------------|------------|----------------|
| Dismantling/Relocation Existing Metering Suban to Rawa Station | Plant      | I/E            |
| Suban-5 SRU (Solid Removal Unit) Installation                  | Suban Well | Mech, I/E, OPS |




## 6. PM / CM CONTROL SUMMARY

Routine PM/CM is managed through SAP PM and weekly planning. This section only captures PM/CM with cross-functional or operational impact.

| Type          | Area  | Impact            | Control Action       |
|---------------|-------|-------------------|----------------------|
| 4K GTC-500 PM | Suban | Production Impact | Execution as planned |

## 7. RESOURCE & CRAFT UTILIZATION

| Area  | Craft      | Utilization (%) | Status (Normal / Overload) | Action |
|-------|------------|-----------------|----------------------------|--------|
| Suban | Electrical | 97              | Normal                     |        |
| Suban | Instrument | 100             | Normal                     |        |
| Suban | Mechanical | 94              | Normal                     |        |

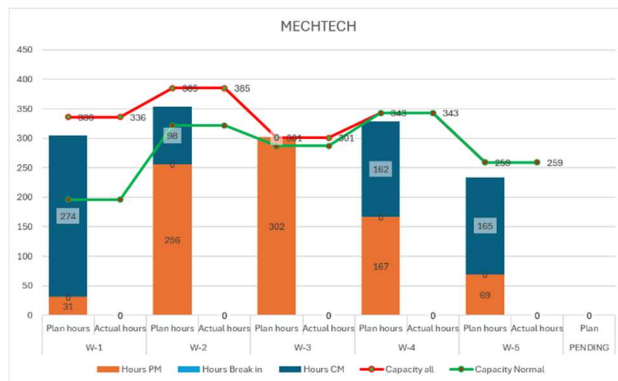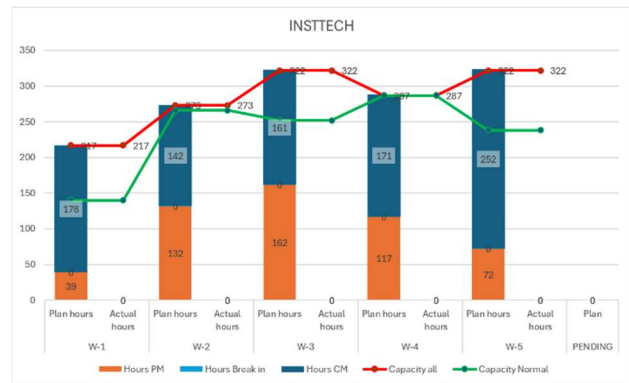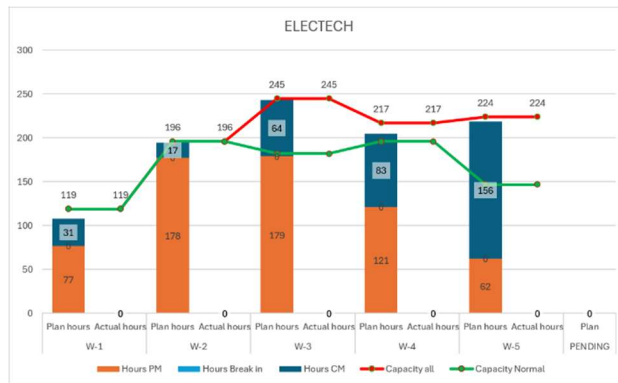

## 8. SUBAN VISITS, AUDITS & EXTERNAL EVENTS

| No. | Event                                                            | Personnel                                                                                                                                   | Visit Start | Visit End | Operational Impact                                                          | Control / Mitigation                             |
|-----|------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------|-------------|-----------|-----------------------------------------------------------------------------|--------------------------------------------------|
| 1   | Witness Audit (General Audit)                                    | Hadi Thamin                                                                                                                                 | 01-Jul-26   | 03-Jul-26 | POB increase presence of visitors may affect routine operational activities | Implement POB monitoring.                        |
| 2   | Combined General Audit Corridor and Internal Audit ABMS Corridor | 1. Soesetyo Eri Perbowo<br>2. Deny Pardede<br>3. Lovidya Helmi<br>4. Novrisima Eva Sianturi<br>5. Monica Aristadewi Adisasmita (1 Jul 2026) | 29-Jun-26   | 03-Jul-26 | POB increase presence of visitors may affect routine operational activities | Implement POB monitoring.<br>Implement Corredja. |
| 3   | Evaluasi Mutu Minyak dan Gas Bumi                                | 1. Yudha Saputra (LEMIGAS)<br>2. Iqbal Wardana (LEMIGAS)<br>3. TBN (SKK Migas)<br>TBN (MEPG)                                                | 06-Jul-26   | 07-Jul-26 | POB increase                                                                | Implement POB monitoring.                        |
| 4   | Kunjungan tim QA QC                                              | 1. Iman Sugihartoto<br>2. Ahmad Sultani<br>4. Piter Sipayung                                                                                | 13-Jul-26   | 15-Jul-26 | POB increase                                                                | Implement POB monitoring.                        |

|   |                                                                          |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |           |           |                                                                             |                                                |
|---|--------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------|-----------|-----------------------------------------------------------------------------|------------------------------------------------|
| 5 | Visitation Team OI                                                       | 1. Anthonia Yasmine<br>2. Alisia Azzahra<br>3. Annisa Deviana                                                                                                                                                                                                                                                                                                                                                                                                                        | 13-Jul-26 | 14-Jul-26 | POB increase                                                                | Implement POB monitoring.                      |
| 6 | Coaching Clinic (Sport Trainer)                                          | 1. Trainer<br>2. Internal<br>3. Internal                                                                                                                                                                                                                                                                                                                                                                                                                                             | 18-Jul-26 | 20-Jul-26 | POB increase                                                                | Implement POB monitoring.                      |
| 7 | Evaluasi Mutu Minyak dan Gas Bumi                                        | 1. Adhe Mulat Kusumahi (LEMIGAS)<br>2. TBN (SKK MIGAS)<br>3. TBN (MEPG)                                                                                                                                                                                                                                                                                                                                                                                                              | 22-Jul-26 | 23-Jul-26 | POB increase.                                                               | Implement POB monitoring.                      |
| 8 | Pembuatan Video dan Foto Dokumentasi Community Enhancement Blok Corridor | Charprod:<br>1. Charis Yudho<br>2. Rendra Hernawan<br>3. M. Rizal, Hari Septiandoko<br>Medco:<br>3. Feddy Fahdi                                                                                                                                                                                                                                                                                                                                                                      | 26-Jul-26 | 29-Jul-26 | POB increase.                                                               | Implement POB monitoring.                      |
| 9 | Asset HSE Compliance Audit - Suban (AssetHSE202607)                      | 1. Kimberly Audrey (Coordinator HSEMS & Audit Compliance Corridor)<br>2. Lucky R. Ferdiyawan (Manager Performance Assurance & Audit Corridor)<br>3. dr. Rony Catur Wibowo (Manager Occupational Health & Industrial Hygiene – HSE Corporate)<br>4. Ari Widodo (Specialist Process Safety Corridor)<br>5. Hendra Andriadi (Lead Asset Integrity Corridor)<br>6. Indah Lestari (Project Electrical Engineer)<br>7. Hilal T. Prakhasa (Manager Environment Stewardship – HSE Corporate) | 26-Jul-26 | 31-Jul-26 | POB increase presence of visitors may affect routine operational activities | Implement POB monitoring. Implement Corredeja. |

### 9. MOC, Process Safety & Non-Process Safety Action Plan – Follow up in July 2026

| Item | Title & Description PS                                                      | Responsible Person   | Due in  | FOLLOW UP ACTION                                              |
|------|-----------------------------------------------------------------------------|----------------------|---------|---------------------------------------------------------------|
| MOC  | Install new N2 Generator Package in Suban Plant. PID: 9053055               | Joko Turut Utomo     | Overdue | Follow up to document review by Supt. OCS                     |
| MOC  | Dismantling Equipment transfer for TCMS Project (Tengah Comp). PID: 9532465 | Hamzah Furqoni Zuhdi | Overdue | Follow up to corrective action review closure by MMS Engineer |

|      |                                     |                      |                  |                                                              |
|------|-------------------------------------|----------------------|------------------|--------------------------------------------------------------|
| MOC  | Rental Solid Removal Unit for SB-05 | Hamzah Furqoni Zuhdi | 29 November 2026 | Follow up corrective action by Engineer Process Surveillance |
| IAAN | IAAN - Suban #8 (KP 6+322)          | Said G. / Hefni A.   | 5 March 2027     | Coating Repair                                               |

## 9. COST & BUDGET ALIGNMENT

| Budget Owner     | FC 4+8 LTP   | Actual 4+8   | Risk / Remarks                                                                                                                                                                                                        |
|------------------|--------------|--------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Operations       | USD 0.166 MM | USD 0.167 MM | within budget                                                                                                                                                                                                         |
| Maintenance      | USD 0.184 MM | USD 0.184 MM | Within budget                                                                                                                                                                                                         |
| Support Services | USD 0.290 MM | USD 0.218 MM | (40K) : Released Accrual March but actual not yet post on May<br>(20K) : Delay Activity for Constructed GS Storage and Concreted Walkway to Block D<br>(16K) : Wrong Charge Standby by Crane 80 T for march and April |
| Pipeline & ROW   | USD 0.071 MM | USD 0.090MM  | FX difference                                                                                                                                                                                                         |
| Road Maintenance | USD 0.090 MM | USD 0.084 MM | FX difference                                                                                                                                                                                                         |

## 10. CHANGE CONTROL LOG (BREAK-IN)

Any change to a Frozen 30D Plan must be formally recorded and approved.

| Date | Change Description | Impact | Approved By |
|------|--------------------|--------|-------------|
| -    | -                  | -      | -           |

Note: This Change Control Log shall be completed **during the month of execution** and updated **whenever a break-in occurs** for monitoring and governance purposes

## 11. 30D PERFORMANCE SUMMARY (PREVIOUS MONTH) Updated 29 June 2026

| Indicator            | Result | Remarks                         |
|----------------------|--------|---------------------------------|
| Plan Attainment      | 84%    |                                 |
| Plan Stability       | 86%    | Meet Target                     |
| Total Activities     | 971    |                                 |
| Addition to Plan     | 72     | Break-in Activity               |
| Deletion from Plan   | 131    | Postpone, Cancel and Carry Over |
| On Schedule          | 840    | Completed and InProgress        |
| Completed Activities | 816    |                                 |

Note:

- Plan Attainment represents the percentage of approved and frozen 30D activities that are successfully completed within the agreed execution window and scope. Break-in activities and deferred or cancelled activities are excluded from this calculation.
- Plan Stability represents the percentage of approved and frozen 30D activities that remain unchanged throughout the execution month. Any addition (break-in), deletion, or significant rephrasing of frozen activities is considered a change and will reduce the Plan Stability score.
  - **≥ 90%:** Excellent execution performance with high delivery reliability.
  - **85–89%:** Good and acceptable execution performance; operations remain healthy.
  - **75–84%:** Marginal execution performance; improvement is required.
  - **< 75%:** Poor execution performance with high delivery risk.



### Highlight Previous Month

| No | Activity                                                                                                                                                         | Category<br>(Ops /<br>Maintenance<br>/ Offsite) | Area  | Job Owner                                          | Start Date | End Date | Remark                                                     |
|----|------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------|-------|----------------------------------------------------|------------|----------|------------------------------------------------------------|
| 1  | 258PVS901<br>Produce Water Tank<br>101 Broken                                                                                                                    | Maintenance<br>(Instrument)                     | Suban | Supt.<br>Maintenance<br>Suban                      | 1 June     | 15 June  | Completed                                                  |
| 2  | Suban 24 New<br>Flowline. Welding<br>includes Hot Tap,<br>trenching, lowering<br>pipeline, concrete<br>foundation, install &<br>lifting pipe and<br>install ICCP | Operation<br>(Project)                          | Suban | Project<br>Manager<br>Suban Wellsite<br>& Flowline | 1 June     | 30 June  | InProgress 77%                                             |
| 3  | Suban-34 Surface<br>Facility Construction<br>and First Gas                                                                                                       | Operation<br>(Project)                          | Suban | Project<br>Manager<br>Suban Wellsite<br>& Flowline | 1 June     | 15 June  | Completed                                                  |
| 4  | Observation Well<br>(Sumur Pantau) SP-1                                                                                                                          | Offsite<br>(IDSSMCVL)                           | Suban | Supt. Offsite<br>Suban                             | 1 June     | 30 June  | InProgress 82%                                             |
| 5  | 30000 HRS-<br>23SAE300 SUBAN<br>CAMPAIGN PM                                                                                                                      | Maintenance<br>(Campaign)                       | Suban | Lead Campaign<br>Team                              | 9 June     | 19 June  | Completed                                                  |
| 6  | Sakakemang Project.<br>Dismantle Inlet<br>Separator and<br>accessories                                                                                           | Operations<br>(IDOCs)                           | Suban | Supt.<br>Construction<br>Corridor                  | 17 June    | 30 June  | Continuing prework<br>activity                             |
| 7  | Suban Well (DM#2,<br>Suban 10, Suban 11,<br>dan Suban #4).<br>Instrument Gas<br>System Project.                                                                  | Operations<br>(IDOCs)                           | Suban | Supt.<br>Construction<br>Corridor                  | 1 June     | 10 June  | Completed                                                  |
| 8  | Suban-7<br>Optimization. Install<br>modification spool                                                                                                           | Operations<br>(IDOCs)                           | Suban | Supt.<br>Construction<br>Corridor                  | 17 June    | 30 June  | Completed 1 of 2<br>injection quills.<br>Continue activity |

|    |                                                              |                    |       |                             |         |         |                                                                                |
|----|--------------------------------------------------------------|--------------------|-------|-----------------------------|---------|---------|--------------------------------------------------------------------------------|
|    | existing for tapping KOH.                                    |                    |       |                             |         |         |                                                                                |
| 9  | Suban-5 SRU (Solid Removal Unit) Installation                | Operations (IDOCs) | Suban | Supt. Construction Corridor | 17 June | 30 June | Defer to July                                                                  |
| 10 | Relocation Suban Condensate Metering for ASM project phase#2 | Operations (IDOCs) | Suban | Supt. Construction Corridor | 17 June | 30 June | Defer to July<br>Waiting readiness from RAWA (construction, fabrication spool) |
| 11 | Suban-28 Add Perf & Acidizing                                | Operations (WII)   | Suban | Supt. Well Maintenance Area | 1 June  | 30 June | Completed                                                                      |
| 12 | Suban-13 Acidizing                                           | Operations (WII)   | Suban | Supt. Well Maintenance Area | 15 June | 30 June | Defer to July                                                                  |

## 12. APPROVAL & COMMITMENT

By approving this document as a Frozen 30-Day Operations Plan, all relevant parties commit to execute the listed activities in accordance with the approved plan.

| Name                                                | Position                           | Signature                                                                                           | Date         |
|-----------------------------------------------------|------------------------------------|-----------------------------------------------------------------------------------------------------|--------------|
| M. Huda / Temmy H.                                  | Activity Planner                   | <br>Huda           | 29 June 2026 |
| Ferry O. / A. Tazkir                                | Offsite Planner                    |                    | 29 June 2026 |
| M. Harry K. / Sandy I.<br>/ Buchori (DoA)           | Supt. Plant                        | <br>Sandy Irawanto | 29 June 2026 |
| Elon S. / Aditama<br>/ Anas F. (DoA)                | Supt. Maintenance                  |                    | 29 June 2026 |
| Vicky T. / Bakti K. /<br>Hefni A. (DoA)             | Supt. Offsite                      |                    | 29 June 2026 |
| Haryanto / M. Azis                                  | Supt. Project Suban                |                  | 29 June 2026 |
| Andes B. / Wisnu A.                                 | Supt. Well<br>Maintenance          |                   | 29 June 2026 |
| Ade Anwar / Widlono<br>/ Bagaskoro /<br>Subijantoro | Supt. OCS / Coord. OCS             | <br>Ade Anwar     | 29 June 2026 |
| P. Aryadika /<br>Abdurrahmat H.                     | Mgr. Operations<br>Installation    | <br>P. Aryadika  | 29 June 2026 |
| M. Nurdin / Syarif B.                               | Mgr. Offsite & Support<br>Services | <br>M. Nurdin   | 29 June 2026 |
